



EXTERIOR PHOTO

Looking South (North Elevation)



EXTERIOR PHOTO





Looking North (South Elevation)






INTERIOR PHOTO

- Dryland
- Meeting Rooms
- Wachter Rink









INTERIOR PHOTO

- Schaumberg Rink
- New Lobby
- Locker room corridor





CONSTRUCTION

Schedule

- Construction is on schedule
- Substantial Completion set for November 16, 2017

Current Activities

- Piping ice floor and connecting equipment
- Framing on second floor mezzanine
- Finishing masonry in locker rooms
- Roofing over mezzanine
- Plumbing piping in locker rooms
- Electrical getting ready for permanent power




INTERIOR PHOTO

- Curling Rink
- Rink I





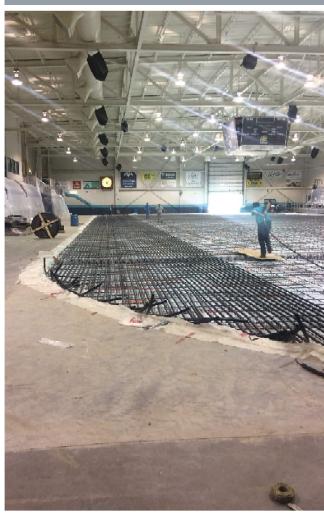

CONSTRUCTION

Schedule

- Construction is on schedule
- Substantial Completion set for September 1, 2017

Current Activities

- Curling rink piping complete, ready to pour
- Rink I Heating piping complete
- Rink I Insulation complete
- Rink I Piping to be complete July 23rd
- Curling Rink and Rink I will be poured July 26th and 27th
