



CAPITAL ICE COMPLEX




BISMARCK PARKS AND RECREATION DISTRICT



EXTERIOR PHOTO

LOOKING NORTH (SOUTH ELEVATION)

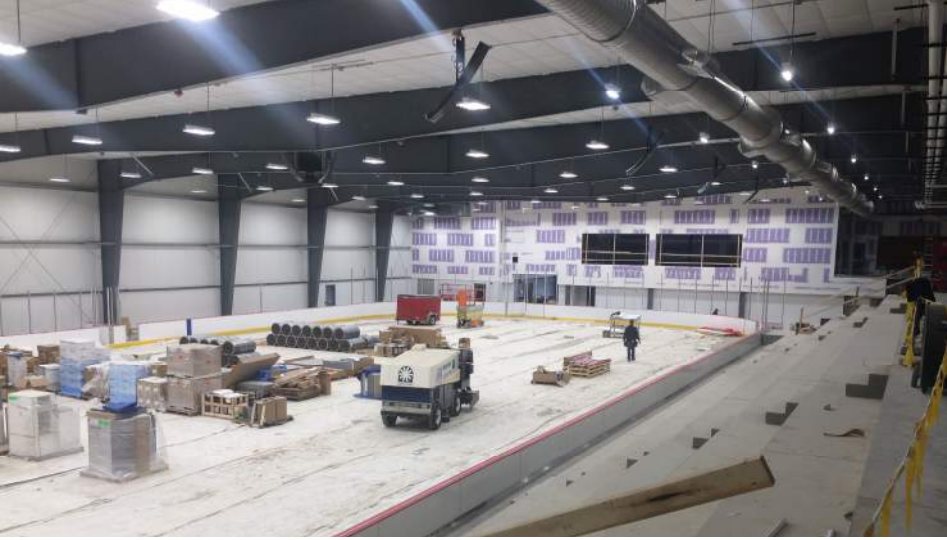


INTERIOR PHOTO

- Top left: Wachter Rink
- Middle: mezzanine to Schaumberg Rink
- Right: Mezzanine



INTERIOR PHOTO

- Top left: looking towards mezzanine
- Top right: Schaumberg Rink
- Bottom right: Locker room on old lobby

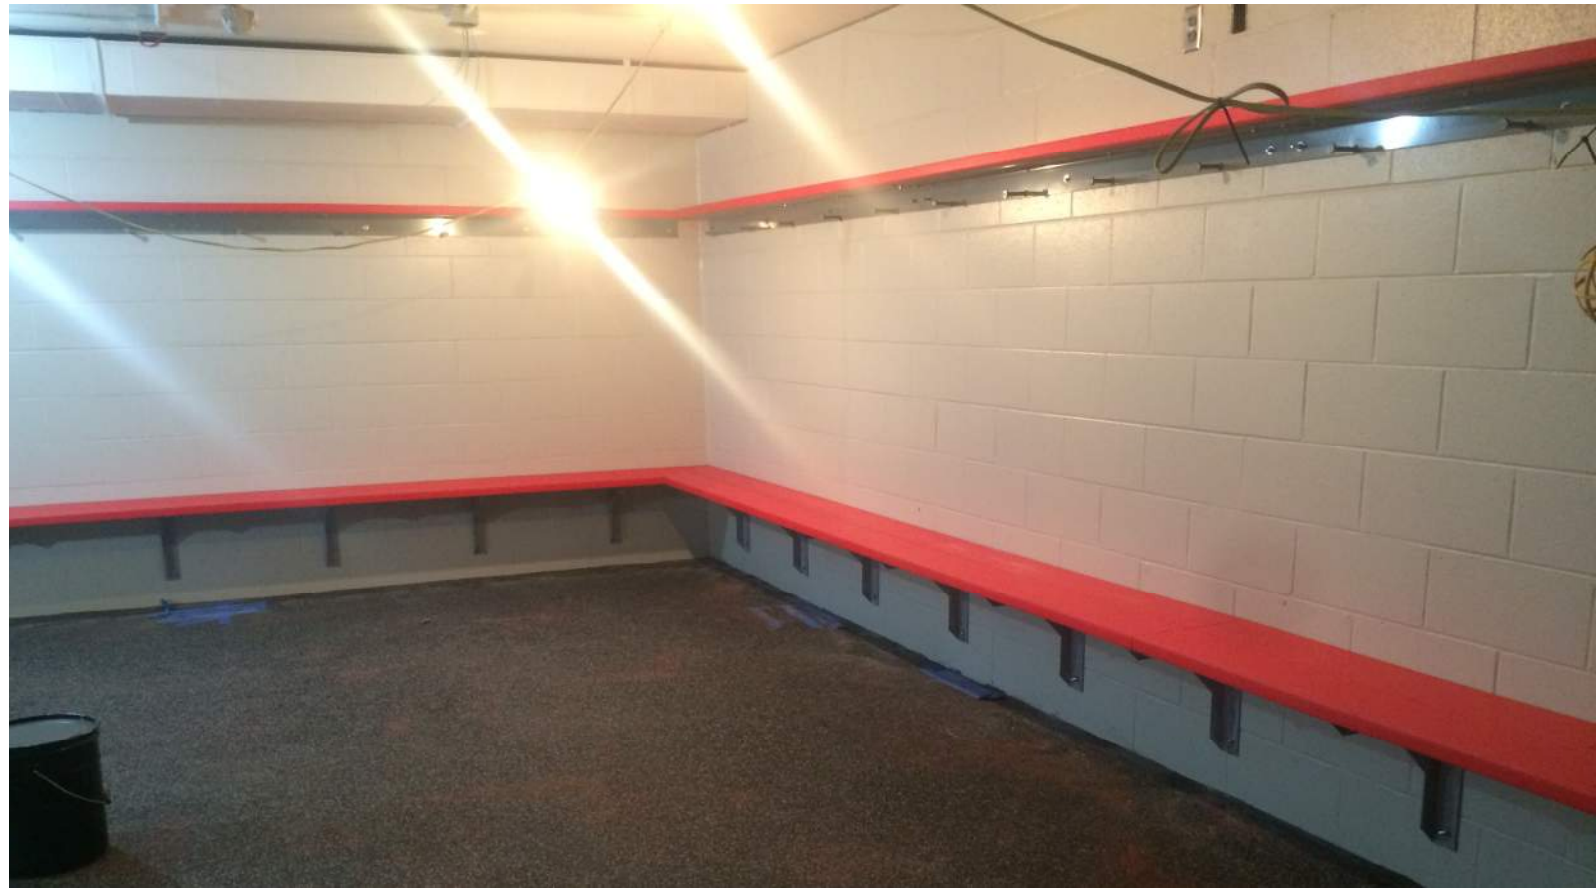

CONSTRUCTION

Schedule

- Construction is tracking.
- Substantial Completion set for November 16, 2017
- Schaumburg Rink will be ready October 23rd

Current Activities

- Tape, texture and painting
- Dasher board installation on-going
- Installing rubber flooring
- Installing floor tile
- Trimming out electrical work
- Hanging plumbing fixtures
- Commissioning and start-up of mechanical equipment.
